AGI INFRA LTD.
(BUILDERS & DEVELOPERS)
CIN : L45200PB2005PLC028466
Jalandhar Heights, 66 Ft. Road, Village Pholriwal, Near Urban Estate Phase-II, Jalandhar City (Punjab) INDIA
Phone : 0181-2681986 | Tel/Fax : 0181-2681886 | gi_builders@yahoo.co.in
info@agiinfra.com | www.agiinfra.com

Date: July 03, 2020

The Advisor
Ministry of Environment, Forest & Climate Change
Northern Regional Office
Bays No. 24-25, Sector 31-A
CHANDIGARH.

SIR

Sub.: Submission of compliance of EC of "*AGI Smart Homes, Jalandhar*"

We are developing an affordable residential apartment complex "AGI Smart Homes" at Village Pholriwal, Tehsil & Distt. Jalandhar.

The project was granted EC by the SEIAA, Punjab, (vide no. SEIAA/2017/504, dated 03.05.2017).

As a part of the statutory requirement, please find enclosed six-monthly compliance report, along with requisite annexures, of the EC of the project.

Hope your good office will find the same in order

With regards

For **AGI Infra Ltd.**

(Authorised Signatory)

SIX-MONTHLY ENVIRONMENTAL COMPLIANCE REPORT

CONSTRUCTION OF RESIDENTIAL APARTMENT COMPLEX "AGI SMART HOMES"

AT

VILLAGE PHOLRIWAL, DISTRICT JALANDHAR PUNJAB.

SUBMITTED BY:

M/S AGI INFRA LTD., C/O JALANDHAR HEIGHTS II, 66 Road, VILLAGE PHOLRIWAL, JALANDHAR.

TABLE OF CONTENTS

S. NO.	DESCRIPTION	PAGE NO.
1.	Data sheet	1-2
2.	Annotated Compliance of Conditions of the EC	3-9
ANNEXURES		
Annexure – I	Environmental Monitoring Reports	10-14
Annexure – II	Site Photographs	15-21

DATA SHEET

<table>
<tr><td>1.</td><td>Project type</td><td>Construction Project</td></tr>
<tr><td>2.</td><td>Name of the project</td><td>AGI Smart Homes</td></tr>
<tr><td>3.</td><td>Clearance letter (S) O.M. No.& Date</td><td>Environment Clearance has been granted vide Letter no. SEIAA/2017/504,dated 03.05.2017.</td></tr>
<tr><td>4.</td><td colspan="2">Location</td></tr>
<tr><td>a.</td><td>District(s)</td><td>Jalandhar</td></tr>
<tr><td>b.</td><td>State(s)</td><td>Punjab (Pb)</td></tr>
<tr><td>c.</td><td>Latitude/Longitude</td><td>75°35'32" N, 31°15'42" E</td></tr>
<tr><td>5.</td><td>Address for correspondence</td><td>M/s AGI Infra Ltd.,
C/o Jalandhar Heights,
66 Road, Village Pholriwal,
Jalandhar.</td></tr>
<tr><td>6.</td><td colspan="2">Salient Features</td></tr>
<tr><td>a.</td><td>Of the project</td><td>The total plot area is ~31125 m^2 (~7.691 acres) and total built up area will be ~120940 m^2.</td></tr>
<tr><td>b.</td><td>Of the Environment Management Plans</td><td>As per the Environmental Clearance, the details are;
<table><tr><td>Water Demand</td><td>760-790 m^3/day</td></tr><tr><td>Water Supply</td><td>Bore well</td></tr><tr><td>Wastewater Treatment</td><td>Proposed STP of capacity ~600 m^3/day</td></tr><tr><td>Solid waste</td><td>The total quantity of solid waste generation (MSW) will be ~2400 kg/day.</td></tr></table></td></tr>
<tr><td>7</td><td colspan="2">Break-up of the project Area</td></tr>
<tr><td>a.</td><td>Submergence area: Forest and Non-Forest</td><td>Not applicable</td></tr>
<tr><td>b.</td><td>Others</td><td>Not applicable</td></tr>
<tr><td>8</td><td>Break up of project affected population with enumeration of those losing houses/dwelling units only, agricultural land only both dwelling units and agricultural land and landless laborers/land landless/artisans.</td><td>No population has been affected as there was no inhabitation on the land.</td></tr>
<tr><td>a.</td><td>SC/ST/Adivasis</td><td>Not applicable</td></tr>
<tr><td>b.</td><td>Others
(please indicate whether these figures are base on any scientific and systematic survey carried out or only provisional figures. If a survey has been carried out give details and year of</td><td>Not applicable</td></tr>
</table>

	survey)	
9	Financial details	
a.	Project cost as originally planned and subsequent revised estimates and the year of price reference.	Total cost of the project is about **₹ 140.44 crores.**
b.	Allocations made for environmental management with item wise and year of assessment.	As per the EC, ~₹ 180 lacs will be incurred on account of capital cost and ~R 62 lacs will be incurred, annually, on account of operational phase for implementation of EMP/CSR.
c.	Benefit cost ratio/Internal rate of return and year of assessment.	Will be submitted
d.	Whether (c) includes the cost of environmental management as shown in (b) above.	Yes. The cost benefit ratio will be worked out considering the cost of environment, as well.
e.	Actual expenditure incurred on the project so far.	~₹ 100 Crores
f.	Actual Expenditure incurred on the EMP so far.	~₹ 95 lacs.
10	Forest lands requirements:	
a.	The status of approval for diversion of forest land for non-forestry use.	As per the NOC issued by Divisional Forest Officer, Jalandhar Forest Division, Phillaur, vide no. 8252, dated 06.01.2017, the project does not attract any forest land or trees.
b.	The status of clear felling, if any	Nil
c.	The status of compensatory afforestation, if any	N.A.
d.	Comments on the viability & sustainability of compensatory afforestation programme in the light of actual field experience so far	__
11	The status of clear felling in no forest areas (such as submergence area of reservoir, approach road) if any, with quantitative information.	Nil
12	Status of Construction	
a.	Date of commencement (actual and/or planned)	06/04/2017
b.	Date of completion (actual and/or planned)	The project is still in construction phase. The planned date of completion is 03/2022.
13	Reasons for the delay, if the project is yet to start:	__

Compliance Report of EC

(*No. SEIAA/2017/504 dated 03.05.2017*)

PART A – Conditions common for all the three phases i.e. Pre-Construction Phase, Construction Phase and Operation Phase & Entire Life		
i)	Any appeal against this environmental clearance shall lie with the National Green tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.	Understood and accepted.
ii)	A first aid room will be provided in the project both during construction and operation phase of the project.	First Aid Room has been provided at the project site. It is being maintained during operation phase of the project. In case of any major medical emergency patients can be shifted to the nearby hospital which is at a distance of ~1.5 km from the project site.
iii)	Construction of the STP, solid waste, e-waste, hazardous waste storage facilities, tubewell, DG sets, utilities, etc., earmarked by the project proponent on the layout plan, should be made in the earmarked area only. In any case, the position/location of these utilities should not be changed later on.	As per the present planning under execution, there is no change in position/location of the utilities from that on submitted layout plans. Besides, if any such change is necessitated, a prior approval of the same will be obtained.
iv)	The environmental safeguards contained in the application of the promoter mentioned during the presentation before State Level Environment Impact Assessment Authority/State Expert Appraisal Committee should be implemented in letter and spirit	The project proponent undertakes to ensure implementation of all relevant submissions and commitments in letter and spirit.
v)	Ambient air & noise levels should conform to prescribed standards both during day and night. Incremental pollution loads on the ambient air quality, noise especially during worst noise generating activities, water quality and soil should be periodically monitored during construction phase as well as operation & entire life phase as per the Ministry of Environment, Forests & Climate Change guidelines and all the mitigation measures should be taken to bring down the levels within the prescribed standards.	The project proponent undertakes to ensure that at no time, incremental pollution loads on ambient air quality noise, water quality and soil, shall not cause any violation of prescribed standards. The environmental quality monitoring is periodically being carried out and shall be continued as per the applicable guidelines.
vi)	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department,	Agreed and undertake to ensure.

	Forest (Conservation) Act, 1980 and Wildlife (Protection) Act, 1972 etc. shall be obtained, by project proponents from the competent authorities including Punjab Pollution Control Board and from other statutory bodies as applicable.	
vii)	The State Environmental Impact Assessment Authority, Punjab, reserves the right to add additional safeguards/measures subsequently, if found necessary, and to take action including revoking of the environmental clearance under the provisions of the Environmental (Protection) Act, 1986, to ensure effective implementation of the suggested safeguards/measures in a time bound and satisfactory manner.	Understood and accepted.
viii)	A proper record showing compliance of all the conditions of environmental clearance shall be maintained and made available at site at all the times.	Agreed and undertake to ensure.
ix)	The project proponent shall also submit half yearly compliance reports in respect of the stipulated prior environmental clearance terms & conditions including results of monitored data (both in hard & soft copies) to the respective Regional Office of MoEF, the Zonal Office of CPCB, the SPCB and SEIAA, Punjab, on 1st June and 1st December of each calendar year.	Agreed and undertake to ensure.
x)	Officials from the Regional Office of Ministry of Environment & Forests, Chandigarh/State Level Environment Impact Assessment Authority/State Level Expert Appraisal Committee/Punjab Pollution Control Board who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities, and documents/ data by the project proponents during their inspection. A complete set of all the documents submitted to State Environment Impact Assessment Authority should be forwarded to the APCCF, Regional Office of Ministry of Environment & Forests, Chandigarh.	Agreed and undertake to ensure. A copy of the complete set of all the documents submitted to the SEIAA, Punjab, for obtaining the EC has been forwarded to the RO, MoEFCC, Chandigarh.
xi)	In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by State Environment Impact Assessment Authority, Punjab	Understood and accepted.
xii)	Environmental clearance is subject to final order of the Hon'ble Supreme Court of India in the matter of Goa Foundation Vs. Union of India in Writ Petition (Civil) No. 460 of 2004 as may be applicable to this project and decisions of any Competent Court, to the extent applicable.	Understood and accepted.

xiii)	The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF&CC, SEIAA, Punjab, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels for all the parameters of NAAQM standards shall be monitored and displayed at a convenient location near the main gate of the company in the public domain	Agreed and being done.
xiv)	The inlet and outlet point of natural drain system should be maintained with adequate size of channel for ensuring unrestricted flow of water.	There is no natural drain-line passing through the project site.
xv)	The unpaved area shall be more than or equal to 20% of the recreational open spaces.	Agreed and the same has been included in the project planning.
xvi)	Environmental Management Cell shall be formed which will supervise and monitor the environment related aspects of the project.	The Environment Management Cell has been formed and it comprises of; • S. Sukhdev Singh, Managing Director • Mr. Ashwani Kant Aggarwal, General Manager • Mr. Saranjit Singh Sahi, Deputy General Manager • Mr. Virender Singh, Project Manager
xvii)	The project proponent will always comply with the road widening condition for an area of 0.3 acres given in CLU granted by Department of Town & Country Planning, Punjab vide letter no. 2985 dated 21.12.2016.	Agreed and undertake to comply.
PART B – Specific Conditions		
(I)	**Pre-construction Phase**	
i)	"Consent to establish" shall be obtained from Punjab Pollution Control Board under Air (Prevention & Control of Pollution) Act, 1981 and Water (Prevention & Control of Pollution) Act, 1974 and a copy of the same shall be submitted to the Ministry of Environment & Forests/State Level Environment Impact Assessment Authority before the start of any construction work at site.	CTE has already been obtained from the PPCB – copy enclosed.
ii)	All required sanitary and hygienic measures should be in place before starting construction activities and to be maintained throughout the construction phase.	The requisite measures has already been put in place and shall be maintained throughout the construction phase.

iii)	The approval of competent authority shall be obtained for structural safety of the buildings due to earthquakes, adequacy of firefighting equipment's etc. as per National Building Code including protection measures from lightning.	All the requisite approvals have been obtained.
iv)	Provision shall be made for the housing of construction labor within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, disposal of waste water & solid waste in an environmentally sound manner, safe drinking water, medical health care, crèche, etc. The housing may be in the form of temporary structures to be removed after the completion of the project.	Most of the labour is local. Temporary housing with adequate facilities have been provided.
(II)	**Construction Phase**	
i)	All the topsoil excavated during construction activities should be stored for use in horticulture/landscape development within the project site.	The top soil excavated during activities has been safely stored and shall be used only for horticulture/landscape within the project site.
ii)	Disposal of muck during construction phase should not create any adverse effect on the neighboring communities and be disposed off after taking the necessary precautions for general safety and health aspects of people with the approval of competent authority. The project proponent will comply with the provisions of Construction & Demolition Waste Rules, 2016. Dust, smoke & debris prevention measures such as wheel washing, screens, barricading and debris chute shall be installed at the site during construction including plastic/tarpaulin sheet covers for trucks bringing in sand & material at the site.	Muck Management Plan has been prepared for the management and disposal of the muck generated keeping in view the general safety and health aspects of people. The construction waste is being reused in the project and is not being discarded.
iii)	Construction spoils, including bituminous material and other hazardous material, must not be allowed to contaminate watercourses and the dump sites for such material must be secured, so that they should not leach into the groundwater.	No hazardous material is expected to be generated other than the used oil from the DG Sets which will be disposed off as per the Hazardous and Other Wastes (Management & Transboundary Movement) Rules, 2016.
iv)	Vehicles hired for bringing construction material to the site and other machinery to be used during construction should be in good condition and should conform to applicable air emission standards.	All the vehicles are less than 10 years old and are periodically validated for PUC certificate and other provisions of the Motor Vehicle Act.
v)	The project proponent shall use only treated sewage/wastewater for construction activities and no fresh water for this purpose will be used. A proper record in this regard should be maintained and available at site.	The construction water requirement is being wholly met through use of treated sewage from Jalandhar Heights, Phase-I. A pipeline has been provided from the STP for this purpose.

vi)	Fly ash based construction material should be used in the construction as per the provisions of Fly Ash Notification of September, 1999 and as amended on August, 2003 and notification No. S.O. 2804 (E) dated 03.11.2009.	The PPC is being extensively used as basic construction material at the site.
vii)	Water demand during construction should be reduced by use of ready mixed concrete, curing agents and other best practices.	An RMC plant is already operational at the site. Other measures are being followed in consultation with the architects.
viii)	The project proponent will provide sewer connectivity at his own cost in case sewer line is not laid to the project site from the main sewer before commissioning of the project.	The PP undertakes to provide sewer connectivity at his own cost in case the same is not made available by the MC.
ix)	Adequate treatment facility for drinking water shall be provided, if required.	Adequate pre-water treatment facility is already in plan for water supply to the inhabitants.
x)	The project proponent shall provide electromagnetic flow meter at the outlet of the water supply, outlet of the STP and any pipeline to be used for re-using the treated wastewater back into the system for flushing and for horticulture purpose/green etc.	Agreed and undertake to comply.
xi)	The project proponent will provide dual plumbing system for reuse of treated wastewater for flushing/HVAC purposes etc. and color coding of different pipe lines carrying water/wastewater/treated wastewater as follows: a) Fresh water – Blue b) Untreated wastewater – Black c) Treated wastewater(for reuse) – Green d) Treated wastewater (for discharge) – Yellow e) Storm water – Orange	Agreed and undertake to comply.
xii)	Fixtures for showers, toilet flushing and drinking should be of low flow either by use of aerators or pressure reducing devices or sensor based control.	Agreed and undertake to comply.
xiii)	Separation of drinking water supply and treated sewage supply should be done by the use of different colors.	Agreed and undertake to comply.

xiv)	a) Adequate steps shall be taken to conserve energy by limiting the use of glass, provision of proper thermal insulation and taking measures as prescribed under the Energy Conservation Building Code and National Building Code, 2005 on Energy conservation. b) Solar power plant by utilizing at least 30% of the open roof top area in the premises shall be installed for utilizing maximum solar energy. Also, LED lights shall.be provided as proposed for illumination of common areas instead of CFL lights or any other conventional lights/bulbs.	Agreed and undertake to comply.
xv)	The diesel generator sets to be used during construction phase should conform to the provisions of Diesel Generator Set Rules prescribed under the Environment (Protection) Act, 1986.	Agreed and undertake to comply.
xvi)	Chute system, separate wet & dry bins at ground level and for common areas for facilitating segregation of waste, collection centre and mechanical composter (with a minimum capacity of 0.3 kg/tenement/day) shall be provided for proper collection, handling, storage, segregation, treatment and disposal of solid waste.	Agreed and undertake to comply.
xvii)	A rainwater harvesting plan shall be designed where the re-charge bores (minimum one per 5000 sq.m. of built up area) shall be provided. Recharging wells for roof top run-off shall have provision of adequate treatment for removing suspended matter etc. before recharging as per the CGWA guidelines. Run-off from areas other than roof top such as green areas and roads/pavement etc. may also be recharged but only after providing adequate treatment to remove suspended matter, oil & grease etc. and ensuring that rainwater being recharged from these areas is not contaminated with pesticides, insecticides, chemical fertilizer etc.	Agreed and undertake to comply.
xviii)	Green belt of adequate width as proposed shall be provided so as to achieve attenuation factor conforming to the day & night standards prescribed for residential land use. The open spaces inside the plot should be suitably landscaped and covered with vegetation of indigenous species/variety. A minimum of one tree for every 80 sq.m. of land shall be planted and maintained. The existing trees may be counted for this purpose. Preference should be given to planting native species. Where the trees need to be cut, compensatory plantation in the ratio of 1:3 (i.e. planting of three trees for every one tree that is cut) shall be done with the obligation to continue maintenance.	Agreed and undertake to comply.

PART C – General Conditions		
(I)	**Pre-construction Phase**	
i)	This environmental clearance will be valid for a period of seven years from the date of its issue or till the completion of the project, whichever is earlier.	Understood and accepted.
ii)	The project proponent should advertise in at least two local newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded environmental clearance and copies of clearance letters are available with the Punjab Pollution Control Board. The advertisement should be made within seven days from the day of issue of the clearance letter and a copy of the same should be forwarded to the Regional Office, Ministry of Environment & Forests, Chandigarh and SEIAA, Punjab.	The EC has been advertised – copies enclosed.
iii)	The project proponent shall obtain permission from the CGWA for abstraction of groundwater & digging of bore well(s) and shall not abstract any groundwater without prior written permission of the CGWA, even if any bore well(s) exist at site	An application has been submitted for obtaining permission for groundwater abstraction from the CGWA.
iv)	The project proponent shall obtain CLU from the competent authority.	The CLU has been obtained – copy enclosed.
v)	A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parishad/Municipal Corporation, Urban local body and the local NGO, if any, from whom suggestions/representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the Company by the proponent.	Copy of the EC has been sent to the MC, Jalandhar. EC letter has also been displayed on the website.
(II)	**Construction Phase**	
i)	The project proponent shall adhere to the commitments made in the Environment Management Plan for the construction phase and Corporate Social Responsibility and shall spend minimum amount of Rs.1.55 crore towards capital investment and Rs. 5 lacs/year towards CSR activities as proposed in addition to the amount to be spent under the provisions of the Companies Act 1956.	Agreed and undertake to comply.

Environ Tech Laboratories

NABL Accredited (ISO/IEC 17025:2017)/ MoEF & CC Recognized
PPCB Approved/ OHSAS 45001:2018

Plot No.62, Janta Industrial Estate,
Airport Road, Sector 82, S.A.S. Nagar
(Mohali)-160062 Punjab
Mob. 9417210081, 9417220081
9464000081, Tel. 9463000081

GSTIN : 03BPEPS9693P1ZV
PAN No. BPEPS9693P

Dispatch No:- ETL/DSP/20777

Dated:- 27/06/2020

TEST REPORT

To
M/s AGI SMART HOMES
(PP-AGI INFRA LTD, JALANDHAR)
VILLAGE PHOLRIWAL, JALANDHAR,
PUNJAB

Report No.	ETL/44/2020/O/20829B	Report Date	27.06.2020
Your Ref. No.	Nil	Type of sample	Borewell Water
Sample Code Given by Customer	Nil	Quantity	10 Liter
		Date of sampling	18.06.2020
Sampling Location	Within Premises	Date of sample receipt	22.06.2020
Sample Collected By	Lab person	Sample I.D.	ETL/32/2020/O/829B
Sampling procedure	As per SOP	Date of test	22.06.2020 – 27.06.2020

	Parameters	Results	Limits of IS: 10500 – 2012		Test method
			Requirement (Acceptable Limit)	Permissible limit in absence of alternate source	
1	pH	7.4	6.5 – 8.5	No relaxation	APHA 23rd Edition:2017 - 4500B
2	Colour, Hazen unit, max	<1	5	25	APHA 23rd Edition:2017-2120B
3	Odour	Agreeable	Agreeable	-----	APHA 23rd Edition:2017-2150
4	Turbidity, NTU max	<1	5	10	APHA 23rd Edition 2017 2130 B
5	Total Dissolved Solids mg/l Max	298	500	2000	APHA 23rd Edition:2017 - 2540 C
6	Alkalinity (as $CaCO_3$) mg/l ,Max	256	200	600	APHA 23rd Edition:2017-2320 B
7	Chloride (as Cl), mg/l, Max	6.5	250	1000	APHA 23rd Edition:2017 - 4500 B
8	Sulphate (as SO_4) mg/l, Max	5.0	200	400	APHA 23rd Edition 2017-4500 E
9	Nitrate (as NO_3) mg/l, Max	1.8	45	No relaxation	APHA 23rd Edition:2017 - 4500 B
10	Fluoride (as F) mg/l Max	0.6	1.0	1.5	APHA 23rd Edition:2017 - 4500 D
11	Calcium (as Ca) mg/l Max	56	75	200	APHA 23rd Edition:2017 - 3500 B
12	Magnesium (as Mg) mg/l, Max	17.1	30	100	APHA 23rd Edition:2017 - 3500 B
13	Total Hardness (as $CaCO_3$) mg/l, Max	210	200	600	APHA 23rd Edition:2017 - 2340 C

NOT VALID FOR LEGAL PURPOSES

Environ Tech Laboratories

NABL Accredited (ISO/IEC 17025:2017)/ MoEF & CC Recognized
PPCB Approved/ OHSAS 45001:2018

Plot No.62, Janta Industrial Estate,
Airport Road, Sector 82, S.A.S. Nagar
(Mohali)-160062 Punjab
Mob. 9417210081, 9417220081
9464000081, Tel. 9463000081

GSTIN : 03BPEPS9693P1ZV
PAN No. BPEPS9693P

Report No. ETL/44/2020/O/20829B	Sample I.D. ETL/32/2020/O/829B

S. No.	Parameters	Results	Limits of IS: 10500 – 2012		Test method
			Requirement (Acceptable Limit)	Permissible limit in absence of alternate source	
14	Chromium (as Cr)mg/L, Max	0.012	0.05	No relaxation	APHA 23rd Edition 2017-3111 B
15	Manganese (as Mn) mg/L, Max	0.003	0.1	0.3	APHA 23rd Edition 2017-3111 B
16	Zinc (as Zn) mg/L, Max	0.25	5	15	APHA 23rd Edition 2017-3111 B
17	Iron (as Fe) mg/l. Max	0.06	0.3	No relaxation	APHA 23rd Edition 2017-3500 B
18	Boron (as B) mg/l. Max	ND	0.5	1.0	APHA 23rd Edition 2017-4500 B
19	Copper (as Cu) mg/L, Max	0.006	0.05	1.5	APHA 23rd Edition 2017-3111 B
20	Lead(as Pb) mg/L, Max	0.006	0.01	No relaxation	APHA 23rd Edition 2017-3111 B
21	Aluminium (as Al) mg/L, Max	ND	0.03	0.2	IS: 3025 (Part 31) : 1964 3500 Al.B
22	Arsenic (as As) mg/L, Max	0.006	0.01	0.05	APHA 23rd Edition 2017-3114 B
23	Selenium(as Se) mg/L, Max	0.006	0.01	No relaxation	APHA 23rd Edition 2017-3114 B
24	Mercury (asHg) mg/L, Max	ND	0.001	No relaxation	APHA 23rd Edition 2017-3112 B
25	Cadmium(as Cd) mg/L, Max	ND	0.003	No relaxation	APHA 23rd Edition 2017-3111 B
26	Residual free chlorine mg/L, Min	0.2	0.2	1	APHA 23rd Edition 2017-4500 B

Bacteriological examination:-

S. NO.	PARAMETERS	TEST RESULTS	LIMITS	TEST METHOD
1	E.coli/100ml	ABSENT	Shall not be detected in any 100 ml of sample	IS 15185: 2016
2	Coliform /100ml	ABSENT		IS 15185: 2016

ND: denotes Not Detectable

All tested parameters are within permissible limit as per IS 10500:2012, so water is potable.

Note:

1. The test report refers only to tested sample and applicable parameters.
2. This report can neither be used as evidence in the court of law nor can it be used in part or full in any media without prior permission.
3. The sample will be destroyed after thirty days from the date of issue of test report unless otherwise specified.

Checked By

****End of Report****

(Authorized Signatory)

AJEET SINGH
Dy. Technical Manager
Environ Tech Laboratories

NOT VALID FOR LEGAL PURPOSES

Environ Tech Laboratories

NABL Accredited (ISO/IEC 17025:2017)/ MoEF & CC Recognized
PPCB Approved/ OHSAS 45001:2018

Plot No.62, Janta Industrial Estate,
Airport Road, Sector 82, S.A.S. Nagar
(Mohali)-160062 Punjab
Mob. 9417210081, 9417220081
9464000081, Tel. 9463000081

GSTIN : 03BPEPS9693P1ZV
PAN No. BPEPS9693P

Dispatch No: ETL/DSP/ 20777

Date: 27/06/2020

TEST REPORT

To
M/s AGI SMART HOMES
(PP-AGI INFRA LTD, JALANDHAR)
VILLAGE PHOLRIWAL, JALANDHAR,
PUNJAB

Report No.	ETL/44/2020/0/20829H	Report Date	27.06.2020
Your Ref.No	Ni	Type of sample	Ambient Air Monitoring
Sample Code given by Customer	Nil	Date of Sampling	18.06.2020 - 19.06.2020
Sampling Location	Within Premises	Date of Sample Receipt	22.06.2020
Sample Collected by	Lab Person	Sample I.D.	ETL/32/2020/0/829H
Sampling procedure	As Per SOP	Date of Test	22.06.2020 – 27.06.2020

TECHNICAL DATA

1	Location of Sampling Station	Near Main Gate
2	Instrument Used for Sampling	Respirable Dust Sampler, $PM_{2.5}$ Sampler,
3	Source of Sampling	Ambient Air Monitoring
4	Temperature of Sampling Location	38°C
5	Environmental Condition	Max temp. 41°C Min temp. 29°C Clear Sky
6	Flow Rate of Sampling	0.2 LPM
7	Time Period for Sampling	1440min.

Sr.No.	PARAMETERS	RESULTS	STANDARD	TEST METHOD
1.	PM_{10}	73.6	100.0 µg/m³	IS:5182(P-23):2006, Reaffirmed 2017
2.	SO_2	7.8	80.0 µg/m³	IS:5182(Pt-2):2001, Reaffirmed 2017
3.	NO_2	16.2	80.0 µg/m³	IS:5182(Pt-6):2006, Reaffirmed 2017
4.	$PM_{2.5}$	42.0	60.0 µg/m³	SOP (ETL/SOP/02- Section-4)
5.	CO (1 hour)	ND	4.0 mg/m³	IS:5182 (P-10)
6.	Nickel (Ni)	ND	20.0 ng/m³	Lab. SOP (BY AAS)
7.	Arsenic (As)	ND	6.0 ng/m³	Lab. SOP (BY AAS)
8.	Lead (Pb)	ND	1.0 µg/m³	Lab. SOP (BY AAS)
9.	Benzene (C_6H_6)	ND	5.0 µg/m³	Lab. SOP (BY G.C)
10.	Benzo (a) pyrene (Ba P)	ND	1.0 ng/m³	Lab. SOP (BY G.C)
11.	Ammonia (NH_3)	ND	400.0 µg/m³	CPCB Guideline
12	Ozone (O_3)	ND	60.0 µg/m³	CPCB Guideline

ND denotes not detectable

Note:

1. The test report refers only to tested sample and applicable parameters.
2. This report can neither be used as evidence in the court of law nor can it be used in part or full in any media without prior permission.
3. The sample will be destroyed after thirty days from the date of issue of test report unless otherwise specified.

(Checked By)

****End of Report****

(Authorized Signatory)
AMEET SINGH
Dy. Technical Manager
Environ Tech Laboratories

Environ Tech Laboratories

NABL Accredited (ISO/IEC 17025:2017)/ MoEF & CC Recognized
PPCB Approved/ OHSAS 45001:2018

Plot No.62, Janta Industrial Estate,
Airport Road, Sector 82, S.A.S. Nagar
(Mohali)-160062 Punjab
Mob. 9417210081, 9417220081
9464000081, Tel. 9463000081

GSTIN : 03BPEPS9693P1ZV
PAN No. BPEPS9693P

Dispatch No: ETL/DSP/20777

Date: 27/06/2020

TEST REPORT

To
M/s AGI SMART HOMES
(PP-AGI INFRA LTD, JALANDHAR)
VILLAGE PHOLRIWAL, JALANDHAR,
PUNJAB

Report No.	**ETL/44/2020/O/20829I**	**Report Date**	**27.06.2020**
Your Ref. No	**NIL**	Type of sample	**Ambient Noise Level**
Sample Code given by Customer	NIL	Date Monitoring	18.06.2020 - 19.06.2020
Sampling Location	**Near Main Gate**	Sample I.D.	ETL/32/2020/O/8291
Sample Monitored By	Lab Person		
Sampling procedure	As per SOP		

S. NO.	Site	Time of sampling		Result dB(A) Leq		Test method
		Day	Night	Day Time (Limits 65 dB(A)Leq as per noise rule 2000)	Night Time (Limits 55 dB(A)Leq as per noise rule 2000)	
1.	Near Main Gate	11:15am to12:15pm	11:30pm to12:30am	63.8	52.8	IS:9989 Reff.2001

Note:

1. The test report refers only to tested sample and applicable parameters.
2. This report can neither be used as evidence in the court of law nor can it be used in part or full in any media without prior permission.

(Checked by)

(Authorized Signatory)
AJEET SINGH
Dy. Technical Manager
Environ Tech Laboratories

End of Report

Environ Tech Laboratories

NABL Accredited (ISO/IEC 17025:2017)/ MoEF & CC Recognized
PPCB Approved/ OHSAS 45001:2018

Plot No.62, Janta Industrial Estate,
Airport Road, Sector 82, S.A.S. Nagar
(Mohali)-160062 Punjab
Mob. 9417210081, 9417220081
9464000081, Tel. 9463000081

GSTIN : 03BPEPS9693P1ZV
PAN No. BPEPS9693P

DISPATCH No:-ETL/DSP/ 20777

Date:- 27/06/2020

TEST REPORT

To
M/s AGI SMART HOMES
(PP-AGI INFRA LTD, JALANDHAR)
VILLAGE PHOLRIWAL, JALANDHAR,
PUNJAB

Report No.	ETL/44/2020/0/20829Q	Report Date	27.06.2020
Your Ref. No.	NIL	Type of Sample	Soil Sample
Sample Code given by Customer	NIL	Quantity	3 Kg
Sampling Location	Within Premises	Date of Sampling	18.06.2020
Sample Collected by	Lab Person	Date of Sample Receipt	22.06.2020
Sampling procedure	As Per SOP	Sample I.D.	ETL/32/2020/0/829Q
		Date of Test	22.06.2020 – 27.06.2020

Sr.No	PARAMETERS	UNITS OF MEASUREMENT	RESULT	TEST METHODS
1	Moisture Content	%	10.1	USDA:1954-Reaffirmed 2010, IS 2720(Pt-2)(RA 2002)
2	Bulk Density	gm/cc	1.48	USDA:1954- (RA 2010)
3	Water Holding Capacity(WHC)	%	45	USDA:1954 (RA 2010)
4	pH	-----	7.7	IS:2720(Pt.26)2007
5	Conductivity	µS/cm	260	IS:14767:2000
6	Organic Carbon	%	0.20	IS:2720 (Pt-22):2001
7	Available phosphorus/Total phosphorus	Kg/Hectare	0.65	USDA:1954-(RA 20 10)-61
8	Texture	-----	Sandy Clay	USDA:1954/Reaff.2010 Page 30
9	Sand	%	46	USDA:1954/Reaff.2010 Page 30
10	Silt	%	34	USDA:1954/Reaff.2010 Page 30
11	Clay	%	20	USDA:1954/Reaff.2010 Page 30
12	Lead as Pb	mg/kg	ND	DTPA - AAS Method
13	Zinc as Zn	mg/kg	1.7	DTPA - AAS Method
14	Sodium as Na	mg/kg	20	USDA:1954/Reaff.2010 Page 131

Note: ND denotes NOT Detectable

1. The test report refers only to tested sample and applicable parameters.
2. This report can neither be used as evidence in the court of law nor can it be used in part or full in any media without prior permission.
3. The sample will be destroyed after fifteen days from the date of issue of test report unless otherwise specified.

Checked By


(Authorized Signatory)
AJEET SINGH
Dy. Technical Manager
Environ Tech Laboratories

END OF REPORT


AGI SMART HOMES COMPLETE BLOCK-1 (BLOCK-A) PHOTOGRAPH



AGI SMART HOMES COMPLETE BLOCK-2 (BLOCK-B) PHOTOGRAPH

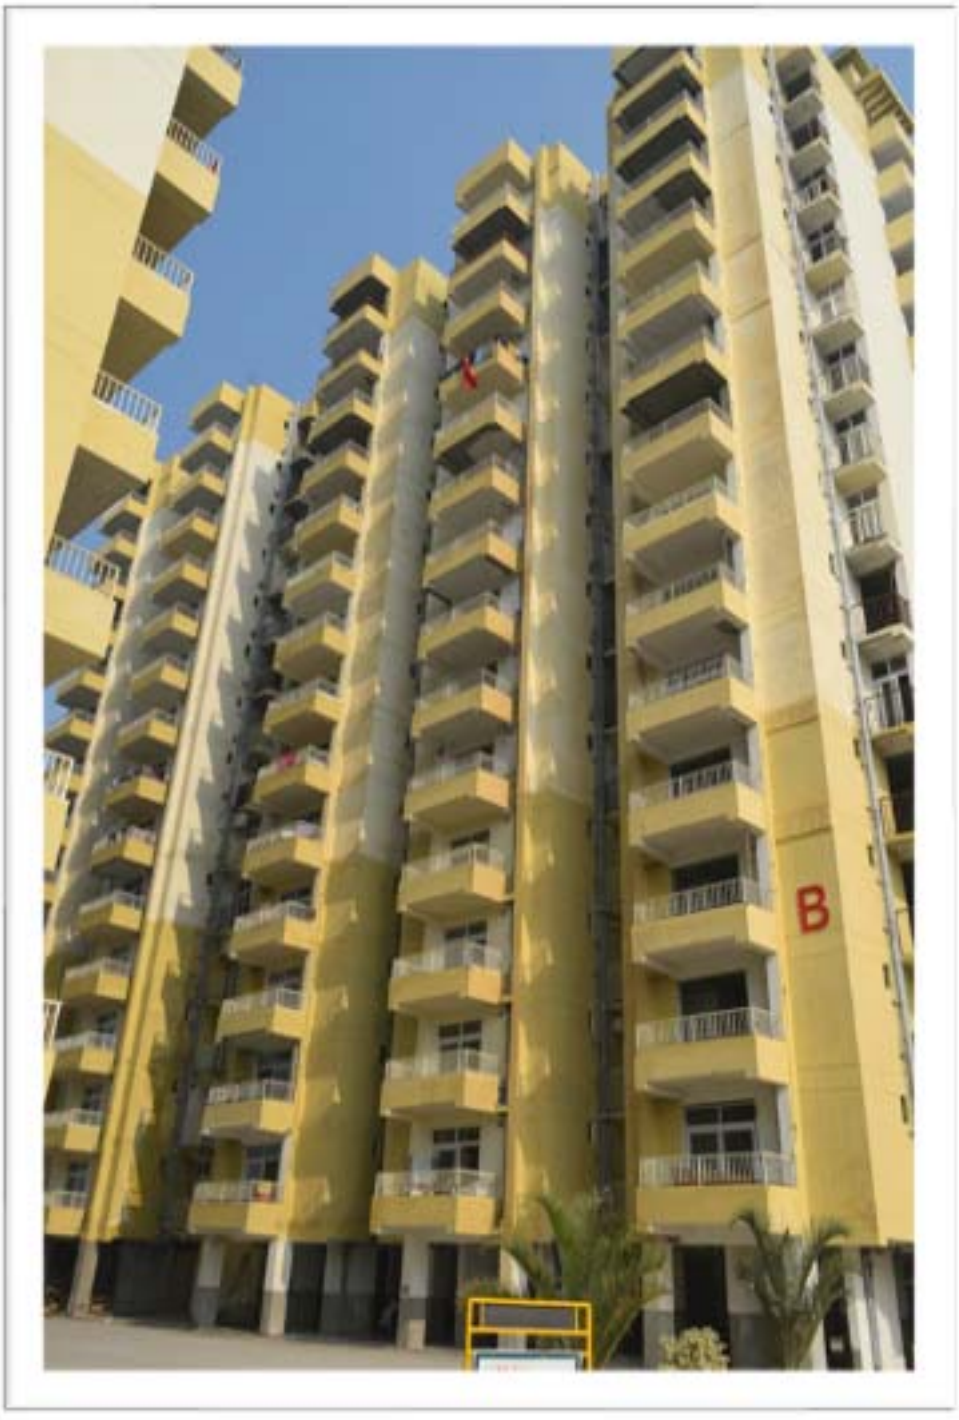

AGI SMART HOMES COMPLETE BLOCK-3 (BLOCK-C) PHOTOGRAPH

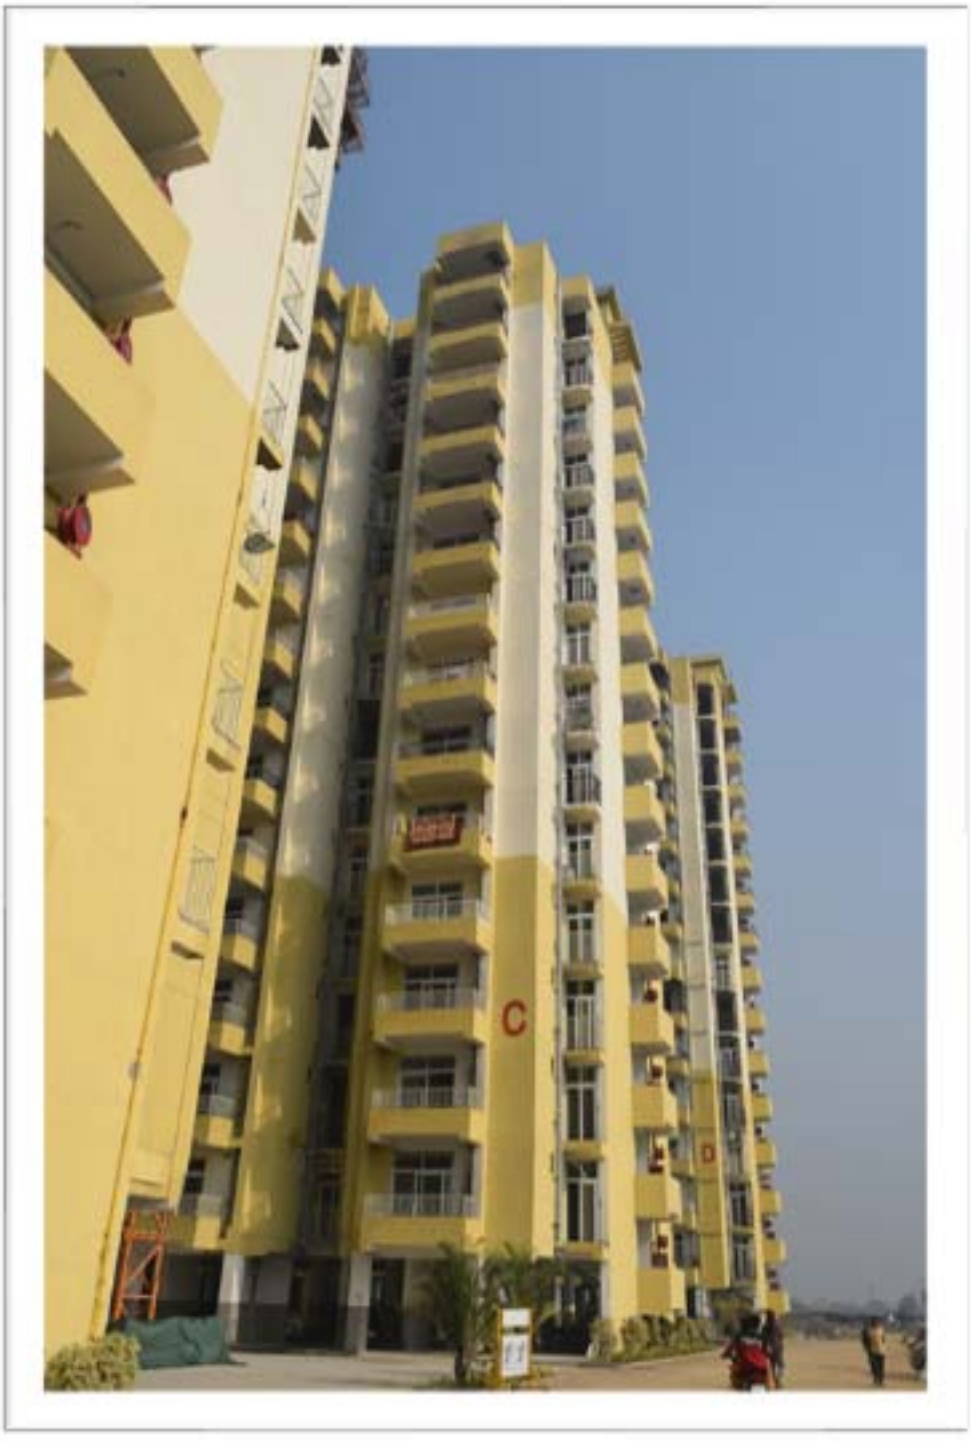

AGI SMART HOMES COMPLETE BLOCK-4 (BLOCK-D) PHOTOGRAPH



PARK PHOTOGRAPH – AGI SMART HOMES



ROAD PHOTOGRAPH – AGI SMART HOMES



FIRE FIGHTING SYSTEM PHOTOGRAPHS – AGI SMART HOMES



(1)



(2)

INTERNAL INFRASTRUCTURE AND COMMON AREAS

SEWERAGE TREATMENT PLAN



(1)



(2)



(3)
